

**Memorandum  
Public Works Department**



**To:** City Manager  
**Subject:** Payment due Valley Construction  
**Date:** March 1, 2023  
**Number:** 2023-044

---

Valley Construction is entitled to payment in the amount of \$51,362.00 for emergency stormwater and sanitary sewer main repairs at the YWCA site on 18<sup>th</sup> Street and 5<sup>th</sup> Avenue. The repair work was done over several days at different times between August and November 2022.

Valley Construction is doing the work at the YWCA and agreed to make these repairs and upgrades on a time and material basis inside their active site.

**Recommendation**

The Public Works Department recommends that the City Council approve the payment to Valley Construction, Rock Island, IL in the amount of \$51,362.00.

Vendor: Valley Construction, Rock Island, IL.  
Payment Amount: \$47,653.00  
Account Chargeable:  
Fund: 506 Sewer Operation & Maintenance  
Division: 619 Utilities Maintenance  
Cost Center: 346 Sewer Collection Maintenance  
Object Code: 53806 Infrastructure Maintenance  
Project Code: 2158000

Payment Amount: \$3,709.00  
Account Chargeable:  
Fund: 507 Stormwater Operation & Maintenance  
Division: 619 Utilities Maintenance  
Cost Center: 348 Stormwater Collection Maintenance  
Object Code: 53806 Infrastructure Maintenance

Requisition Number: R009564

**Submitted by:** Michael T. Bartels, Public Works Director  
Jason Upton, Utilities Superintendent  
Pat O'Brien, Utilities Maintenance Supervisor

---

**Approved by:** Todd Thompson, City Manager



220502

# Invoice

**Bill to:** City of Rock Island, Public Works Dept  
Attn: Public Works Director  
1309 Mill Street  
Rock Island, IL 61201

Invoice Number : 220502  
Contract : 21077-  
Invoice Issue Date :

Cust #	Customer Ref	Billed Through	Due Date	Terms
10228		1/6/2023	1/21/2023	Net due in 15 da

RE : YWCA Sitework and Utilities - Sewer Realignment and Catch Basin T&M Billing

Total Amount Due \$51,362.00

OK - Q.L.J.

# Valley Construction

Invoice Date: January 6, 2023

Valley Job No. 21077  
Phase No. 99-10 & 99-13

For: City of Rock Island  
1309 Mill Street  
Rock Island, IL 61201

Dates Performed: Aug 1-5, 9, Oct 24 & 26, Nov 10, 2022

Description of Work: YWCA Sitework & Utilities - Sewer Realignment & Catch Basin

Labor:	Total S.T. Hours	Total O.T. Hours	Standard Rate	Overtime Rate	Total
Tony Kopf, Laborer Foreman	54.5	4	\$79.53	\$104.08	\$4,750.71
Ken Hurt, Laborer 2	34.5	0	\$75.19	\$97.65	\$2,594.06
Troy Hoffman, Operator 3	54	4	\$99.73	\$125.80	\$5,888.62
James Sawvel, Operator 3	16	0	\$99.73	\$125.80	\$1,595.68
Brady Hill, Laborer 1	30.5	0	\$73.74	\$95.51	\$2,249.07
Quenton Gard, Laborer 2	16	0.5	\$75.19	\$97.65	\$1,251.87
<b>Total Labor:</b>	<b>205.5</b>	<b>8.5</b>			<b>\$18,330.00</b>

Equipment Description	Total Hours	Rate	Total
Chevy 2500HD (11151)	58.50	\$30.00	\$1,755.00
Komatsu PC 138 Zeor Swing Excavator (15168)	38.50	\$150.00	\$5,775.00
Cat 420E-ST 4x4 Loader/Extendahoe (14613)	20.50	\$70.00	\$1,435.00
Komatsu PC128US2 Excavator (15172)	14.00	\$90.00	\$1,260.00
<b>Total Equipment:</b>	<b>131.50</b>		<b>\$10,225.00</b>

Subcontract Work	Hours	Rate	Total
Sycamore Creek Trucking - Inv 10309	8.50	\$99.38	\$844.73
Sycamore Creek Trucking - Inv 10432	18.75	\$101.38	\$1,900.88
Sycamore Creek Trucking - Inv 10446	2.00	\$101.38	\$202.76
Sycamore Creek Trucking - Inv 10530	7.25	\$101.38	\$735.01
Sycamore Creek Trucking - Inv 10531	9.25	\$101.38	\$937.77
Crawford Company - Inv 0130050-IN	1.00	\$575.00	\$575.00
<b>Subtotal Subcontract Work</b>			<b>\$5,196.14</b>
Plus 10% of		\$5,196.14	\$519.61
<b>Total Subcontract Work:</b>			<b>\$5,715.75</b>

Material	Unit	Quantity	Price	Total
Hahn Ready Mix - Inv 419119	Ea	1.00	\$511.25	\$511.25
Hahn Ready Mix - Inv 424896	Ea	1.00	\$450.00	\$450.00
Hahn Ready Mix - Inv 426062	Ea	1.00	\$398.75	\$398.75
RiverStone Group - Inv 1149593	Ea	1.00	\$1,335.83	\$1,335.83
Slavish, Inc. - Inv 8124	Ea	1.00	\$1,811.60	\$1,811.60
Slavish, Inc. - Inv 8153	Ea	1.00	\$180.80	\$180.80
Stetson Building Products - Inv 15742654-00	Ea	1.00	\$6.30	\$6.30
Stetson Building Products - Inv 15744050-00	Ea	1.00	\$11.95	\$11.95
Utility Equipment Company - Inv 10099813-000	Ea	1.00	\$956.00	\$956.00
Zimmer & Francescon - Inv 0170375-IN	Ea	1.00	\$7,305.20	\$7,305.20
Zimmer & Francescon - Inv 0170376-IN	Ea	1.00	\$2,224.13	\$2,224.13
Zimmer & Francescon - Inv 0170413-CM	Ea	1.00	-\$1,465.60	-\$1,465.60
Zimmer & Francescon - Inv 0170940-IN	Ea	1.00	\$545.55	\$545.55
Zimmer & Francescon - Inv 0170941-IN	Ea	1.00	\$459.20	\$459.20
Zimmer & Francescon - Inv 0171008-IN	Ea	1.00	\$616.00	\$616.00
Zimmer & Francescon - Inv 0171050-CM	Ea	1.00	-\$485.00	-\$485.00
<b>Subtotal Material</b>				<b>\$14,861.96</b>
Plus 15% of			\$14,861.96	\$2,229.29
<b>Total Material</b>				<b>\$17,091.25</b>

**Invoice Total: \$51,362.00**

3610-78th Avenue West • Rock Island, IL 61201 • (309) 787-0292 • Fax (309) 787-7048

Phone: 309-787-0292  
 Fax: 309-787-7048

EXTRA WORK ORDER

Date: 8-1-22

Basis of Work:  Time & Material  Quote (state ref.)

Location of Work: YWCA Rock Island

Description of Work: remove & replace Sanitary Sewer

Authorization is for:  all work necessary to complete OR  work from \_\_\_\_\_ to \_\_\_\_\_  
 Company Name: City of Rock Island DATE \_\_\_\_\_ By: \_\_\_\_\_ DATE \_\_\_\_\_  
 Note: Do not begin work without authorization. Do not do work beyond authorization period

LABOR	Name	Classification	Reg. Hours	O.T. Hours	D.T. Hours	Comments
		<u>Tony Kopf</u>	<u>Foreman</u>	<u>8</u>	<u>.5</u>	
	<u>Tray Hoffman</u>	<u>Operator</u>	<u>8</u>	<u>.5</u>		
	<u>Ken Hurt</u>	<u>Pipe Setter</u>	<u>8</u>			

EQUIPMENT	Equipment Number	Description	Total Hours	Comments
		<u>11151</u>	<u>Pick up truck</u>	<u>8</u>
	<u>15168</u>	<u>Kom. 138 excavator</u>	<u>8</u>	

MATERIALS	Description (Attach Delivery Slips)	Quantity & Units	Supplier/Source
		<u>Manhole Barrels</u>	<u>2</u>
	<u>ECC. Cones</u>	<u>2</u>	<u>Slavish Inc.</u>

I hereby certify the above labor, equipment, materials, and supplies were used in the performance of this work.  
[Signature] Eng. Tech 1 8-9-22

Labor Hours	8/1/2022 S.T. Hours	8/2/2022 S.T. Hours	8/3/2022 S.T. Hours	8/4/2022 S.T. Hours	8/5/2022 S.T. Hours	8/9/2022 S.T. Hours	10/24/2022 S.T. Hours	10/26/2022 S.T. Hours	11/10/2022 S.T. Hours	Total S.T. Hours
Tony Kopf, Laborer Foreman	8	8	3	8	8	4	6	1.5	8	54.5
Ken Hurt, Laborer 2	8	8	2.5	8	8					34.5
Troy Hoffman, Operator 3	8	8	2.5	8	8	4	6	1.5	8	54
James Sawvel, Operator 3		8			8					16
Brady Hill, Laborer 1		8	2.5	8	8	4				30.5
Quenton Gard, Laborer 2							6	1.5	8	15.5
<b>Total Daily Hours:</b>	<b>24</b>	<b>40</b>	<b>10.5</b>	<b>32</b>	<b>40</b>	<b>12</b>	<b>18</b>	<b>4.5</b>	<b>24</b>	<b>205</b>

Labor Hours	8/1/2022 O.T. Hours	8/2/2022 O.T. Hours	8/3/2022 O.T. Hours	8/4/2022 O.T. Hours	8/5/2022 O.T. Hours	8/9/2022 O.T. Hours	10/24/2022 O.T. Hours	10/26/2022 O.T. Hours	11/10/2022 O.T. Hours	Total O.T. Hours
Tony Kopf, Laborer Foreman	0.5	0.5	0.5	0.5	0.5	0.5	0.5		0.5	4
Ken Hurt, Laborer 2										0
Troy Hoffman, Operator 3	0.5	0.5	0.5	0.5	0.5	0.5	0.5		0.5	4
James Sawvel, Operator 3										0
Brady Hill, Laborer 1										0
Quenton Gard, Laborer 2							0.5			0.5
<b>Total Daily Hours:</b>	<b>1</b>	<b>1</b>	<b>1</b>	<b>1</b>	<b>1</b>	<b>1</b>	<b>1.5</b>	<b>0</b>	<b>1</b>	<b>8.5</b>

Equipment	8/1/2022 Hours	8/2/2022 Hours	8/3/2022 Hours	8/4/2022 Hours	8/5/2022 Hours	8/9/2022 Hours	10/24/2022 Hours	10/26/2022 Hours	11/10/2022 Hours	Total Hours
Chevy 2500HD (11151)	8.5	8.5	3.5	8.5	8.5	4.5	6.5	1.5	8.5	58.5
Komatsu PC 138 Zeor Swing Excavator (15168)	8	8	2.5	8	8	4				38.5
Cat 420E-ST 4x4 Loader/Extendahoe (14613)		8	2.5		8		2			20.5
Komatsu PC128US2 Excavator (15172)							4.5	1.5	8	14
<b>Total Equipment Hours:</b>	<b>16.5</b>	<b>24.5</b>	<b>8.5</b>	<b>16.5</b>	<b>24.5</b>	<b>8.5</b>	<b>13</b>	<b>3</b>	<b>16.5</b>	<b>131.5</b>

Phone: 309-787-0292  
 Fax: 309-787-7048

EXTRA WORK ORDER

Date: 8-2-22

Basis of Work:  Time & Material  Quote (state ref.)

Location of Work: YWCA Rock Island IL.

Description of Work: remove & replace Sanitary Sewer

Authorization is for:  all work necessary to complete OR  work from \_\_\_\_\_ to \_\_\_\_\_

Company Name: City of Rock Island DATE \_\_\_\_\_ By: \_\_\_\_\_ DATE \_\_\_\_\_


Note: Do not begin work without authorization. Do not do work beyond authorization period.

LABOR	Name	Classification	Reg. Hours	O.T. Hours	D.T. Hours	Comments
	Tony Kopf	Foreman	8	.5		
	Troy Hoffman	Operator-3	8	.5		
	Ken Hurt	LABORER Pipe setter	8			
	Brady Hill	Laborer-1	8			
	James Sawvel	operator-3	8			

EQUIPMENT	Equipment Number	Description	Total Hours	Comments
	11151	Pickup truck	8	
	15168	Kom. PC 138	8	
	14613	Loader Backhoe CAT 420	8	
	Hired Dump truck		8 1/4	
	Hired Dump truck		8 1/2	

MATERIAL	Description (Attach Delivery Slips)	Quantity & Units	Supplier/Source
	15" A2000 pipe	<del>2168</del> 168 LF	Zimmers
	15" x 15" Fernco	2	Zimmers
	CM6D rock	41.13 TONS	river stone
	CM7A rock	13.78 TONS	river stone

I hereby certify the above labor, equipment, materials, and supplies were used in the performance of this work.

 Eng. Tech. I

8-9-22

Phone: 309-787-0292  
 Fax: 309-787-7048

EXTRA WORK ORDER Date: 8-3-22

Basis of Work:  Time & Material  Quote (state ref.) \_\_\_\_\_  
 Location of Work: Ywca Rock Island IL  
 Description of Work: remove & replace 15" sanitary sewer for the city of rock island


Authorization is for:  all work necessary to complete OR  work from \_\_\_\_\_ to \_\_\_\_\_  
 Company Name: City of Rock Island By: \_\_\_\_\_ DATE \_\_\_\_\_  
 Note: Do not begin work without authorization. Do not do work beyond authorization period.

LABOR	Name	Classification	Reg. Hours	O.T. Hours	D.T. Hours	Comments
		Tony Kopf	Foreman	3	1.5	
	Troy Hoffman	Operator - 3	2.5	.5		
	Kew Hurt	Laborer Pipe Setter	2.5			
	Brady Hill	Laborer - 1	2.5			

EQUIPMENT	Equipment Number	Description	Total Hours	Comments
		11151	Pick up truck	2.5
	15168	Kom. PC 138	2.5	
	14613	Cat 420 Loader Backhoe	2.5	
	Hired truck	Dump truck	2	
	Hired truck	Dump truck	2.5	

MATERIAL	Description (Attach Delivery Slips)	Quantity & Units	Supplier/Source
		6m6D Rock	26.27 TONS
	48" Flat top sent back egg. cone	1 1 sent back	slavish Inc.

I hereby certify the above labor, equipment, materials, and supplies were used in the performance of this work.

 Eng. Tech 1

Date: 8-9-22

Phone: 309-787-0292  
 Fax: 309-787-7048

EXTRA WORK ORDER

Date: 8-4-22

Basis of Work:  Time & Material  Quote (state ref.)

Location of Work: Rock Island YWCA

Description of Work: remove & replace 15" sanitary sewer for the City of Rock Island

Authorization is for:  all work necessary to complete OR  work from \_\_\_\_\_ to \_\_\_\_\_  
 Company Name: City of Rock Island By: \_\_\_\_\_  
 Note: Do not begin work without authorization. Do not do work beyond authorization period.

LABORER	Name	Classification	Reg. Hours	O.T. Hours	D.T. Hours	Comments
	<u>Tony Kopf</u>	<u>Foreman</u>	<u>8</u>	<u>.5</u>		
<u>Troy Hoffman</u>	<u>Operator - 3</u>	<u>8</u>	<u>.5</u>			
<u>Ken Hurt</u>	<u>Laborer Pixer</u>	<u>8</u>				
<u>Brady Hill</u>	<u>Laborer - 1</u>	<u>8</u>				

EQUIPMENT	Equipment Number	Description	Total Hours	Comments
	<u>11151</u>	<u>Pick up truck</u>	<u>8</u>	
<u>15168</u>	<u>Kom. PC 138</u>	<u>8</u>		
<u>14613</u>	<u>cat 420 Loader backhoe</u>	<u>8</u>		
<u>hired truck</u>	<u>Dump truck</u>	<u>8</u>		
<u>hired truck</u>	<u>Dump truck</u>	<u>7 1/4</u>		
<u>Hired truck</u>	<u>Dump truck</u>	<u>.5</u>		

MATERIAL	Description (Attach Delivery Slips)	Quantity & Units	Supplier/Source
	<u>CM7A</u>	<u>rock</u>	<u>14.51 ton</u>
<u>CM6D</u>	<u>rock</u>	<u>14.60 ton</u>	<u>river stone</u>

I hereby certify the above labor, equipment, materials, and supplies were used in the performance of this work.  
[Signature] Eng. Tech 1 8-9-22

Phone: 309-787-0292  
 Fax: 309-787-7048

EXTRA WORK ORDER Date: 8-5-22

Basis of Work:  Time & Material  Quote (state ref.)  
 Location of Work: Rock Island YWCA  
 Description of Work: remove and replace 15" sanitary sewer for the City of rock Island

Authorization is for:  all work necessary to complete OR  work from \_\_\_\_\_ to \_\_\_\_\_  
 Company Name: Rock Island By: \_\_\_\_\_ DATE \_\_\_\_\_  
 Note: Do not begin work without authorization. Do not do work beyond authorization period.

LABOR	Name	Classification	Reg. Hours	O.T. Hours	D.T. Hours	Comments
		Tony Kopf	Foreman	<del>8.5</del>	.5	
	Troy Hoffmann	operator-3	<del>8.5</del>	.5		
	JAMES SAWVEL	operator-3	8			
	Ken Hurt	Laborer Pipesetter	8			
	Brady Hill	Laborer - 1	8			
	Crawford company DAN Henderson	Plumber	3			

EQUIPMENT	Equipment Number	Description	Total Hours	Comments
		11151	Pickup truck	8
	15168	Kom. 138	8	
	14613	cat 420 Loader Backhoe	8	
	Hired truck	Dump truck	7.74	
	<del>Hired Truck</del>	<del>Dump Truck</del>		

MATERIAL	Description (Attach Delivery Slips)	Quantity & Units	Supplier/Source
		CM6A rock / concrete 3.5 yards Hahn	14.55 tons
	9" casting & LID	2	Zimmers
	6" Quick Seal	3	<del>Zimmers</del>
	6" A 2000 6" FURNGO	<del>4</del> 2.5 LF	Zimmers
	6" A 2000 45° Bends	6	Zimmers

I hereby certify the above labor, equipment, materials, and supplies were used in the performance of this work.  
 Eng. Tehl 8-9-22

VALLEY CONSTRUCTION CO.

Job no. 21077 Phase 99-11

3610 - 78th Avenue West

Rock Island, IL 61201

(Page 1 of 1) OR Page 1 of 1

Phone: 309-787-0292

fax: 309-787-7048

EXTRA WORK ORDER

Date: 8-9-22

Basis of Work:  Time & Material  Quote (state ref.)

Location of Work: Rock Island YWCA

Description of Work: remove & replace 15" sanitary sewer

Authorization is for:  all work necessary to complete OR  work from \_\_\_\_\_ to \_\_\_\_\_

Company Name: City of rock Island

DATE By: \_\_\_\_\_ DATE

Note: Do not begin work without authorization.

Do not do work beyond authorization period.

LABOR	Name	Classification	Reg. Hours	O.T. Hours	D.T. Hours	Comments
	<u>Tony Kopf</u>	<u>Foreman</u>	<u>4</u>	<u>.5</u>		
<u>Troy Hoffman</u>	<u>operator-3</u>	<u>4</u>	<u>.5</u>			
<u>Brady Hill</u>	<u>Laborer-1</u>	<u>4</u>				

EQUIPMENT	Equipment Number	Description	Total Hours	Comments
	<u>11151</u>	<u>pick up truck</u>	<u>4</u>	
<u>15168</u>	<u>Kom. FC138</u>	<u>4</u>		
<u>14613</u>	<u>cat 420 loader back</u>	<u>4</u>		

MATERIALS	Description (Attach Delivery Slips)	Quantity & Units	Supplier/Source

I hereby certify the above labor, equipment, materials, and supplies were used in the performance of this work.

[Signature] Eng. Tech 1

8/9/22



Field Management Professional

# DAILY SUMMARY REPORT

Date: 08/08/2022

Time: 03:38:52 PM

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Monday, 08/01/2022

Foreman ID: 10104  
 Foreman Name: Anthony M Kopf  
 Transferred On: 8/8/2022 3:38:52 PM

Temperature & Weather:

AM: Clear	PM: Clear
High: 0 F	Low: 0 F Precip: 0

Site Hours Worked:

From: 7:00 AM	To: 3:30 PM
Inspector: Quentin Jefferson	

Ground Conditions / Day Type:

Dry	Cal Days: 678
Work Day	Work Days: 27

*What did we do today?*

We started by moving the fence on the east side of the project out 6 feet then we had the backs fill some areas so we had a place to sit after that we started excavating down in the alleyway to expose the existing sewer main and Tee so I can get a flow line elevation shot we had to support a very large phone cable End it took all day to get dug down to the main

*Delays to Work/Project*

None

*Instructions Received*

Replace sewer main for the city of Rock Island

*People Visiting the Job*

Nick Hecker, Quentin Jefferson

*Employee Summary*

Employee ID	Employee Name	Work Class	Regular Time	Over Time
10104	Anthony M Kopf	Laborer Foreman_Kopf	8.00	0.50
16208	Kenneth M Hurt	Laborer Pipesetter (Grp 2)	8.00	0.00
16255	Troy N Hoffman	Operator 150-3 (high level)	8.00	0.50
<b>Total Hours:</b>			24.00	1.00

*Equipment Summary*

Equipment ID	Description	Work Time
11151	Utility Bed Truck EXT Cab	8.00
15168	Zero Swing Excavator - Komatsu PC138	8.00
<b>Total Hours:</b>		16.00

*Today's Quantities*

Cost Code	Description	Quantity Unit	Actual MH	Budgeted MH
99- 10-	Sewer Realignment Note:	0.01 LS	25.00	0.00
<b>Today's Total:</b>			25.00	0.00

**DAILY SUMMARY REPORT**

Date: 08/08/2022  
Time: 03:38:52 PM

Field Management Professional

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Monday, 08/01/2022

*Diary Images*



Transferred: 8/1/2022  
Taken On: Aug 1 2022 8:46AM  
Foreman: Anthony M Kopf  
Description: Had to excavate around large phone line



Transferred: 8/1/2022  
Taken On: Aug 1 2022 8:46AM  
Foreman: Anthony M Kopf  
Description: Had to move Fence out

Daily MH Total:	25.00
Weekly MH Total:	25.00
Monthly MH Total:	25.00
ToDate MH Total:	657.50



QUALITY SINCE 1925

Field Management Professional

# DAILY SUMMARY REPORT

Date: 08/08/2022

Time: 03:48:48 PM

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Tuesday, 08/02/2022

Foreman ID: 10104  
Foreman Name: Anthony M Kopf  
Transferred On: 8/8/2022 3:48:48 PM

Temperature & Weather:

AM: Partly Cloudy PM: Partly Cloudy  
High: 0 F Low: 0 F Precip: 0

Site Hours Worked:

From: 7:00 AM To: 3:30 PM  
Inspector: Quentin Jefferson

Ground Conditions / Day Type:

Dry Cal Days: 678  
Work Day Work Days: 28

### What did we do today?

On the north east corner of the building site we removed one catch basin that was tied into an existing sanitary manhole we also removed the sanitary manhole we are supposed to set a new manhole in its place however Bush was afraid they were going to undermine it when they were putting in their foundation so it was decided that we wouldn't put that manhole and we would just connect to the existing sewer there and run south and then come back later and install that manhole after the foundation is complete we installed 34 linear feet of a 2001 15 inch clay by PVC Furnco at the end of the day we temporary flume to Pipe

### Delays to Work/Project

None

### Instructions Received

Remove and replace 15 inch sanitary sewer

### People Visiting the Job

Nick Hecker, Quentin Jefferson

### Employee Summary

Employee ID	Employee Name	Work Class	Regular Time	Over Time
10104	Anthony M Kopf	Laborer Foreman_Kopf	8.00	0.50
15805	James D Sawvel	Operator 150-3 (high level)	8.00	0.00
16208	Kenneth M Hurt	Laborer Pipesetter (Grp 2)	8.00	0.00
16255	Troy N Hoffman	Operator 150-3 (high level)	8.00	0.50
16328	Brady J Hill	Laborer Appr Yr 1 @ 75%	8.00	0.00
<b>Total Hours:</b>			40.00	1.00

### Equipment Summary

Equipment ID	Description	Work Time
11151	Utility Bed Truck EXT Cab	8.00
14613	4X4 Loader-Extendahoe - CAT 420E	8.00
15168	Zero Swing Excavator - Komatsu PC138	8.00
<b>Total Hours:</b>		24.00

Field Management Professional

# DAILY SUMMARY REPORT

Date: 08/08/2022

Time: 03:48:48 PM

Project ID: 21077-

Daily Diary Date:

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Tuesday, 08/02/2022

*Today's Quantities*

Cost Code	Description	Quantity Unit	Actual MH	Budgeted MH
99- 10-	Sewer Realignment Note:	0.01 LS	41.00	0.00
<b>Today's Total:</b>			41.00	0.00

*Diary Images*



Transferred: 8/2/2022  
 Taken On: Aug 2 2022 2:03PM  
 Foreman: Anthony M Kopf  
 Description: Removing and reinstalling sewer as we went



Transferred: 8/2/2022  
 Taken On: Aug 2 2022 1:47PM  
 Foreman: Anthony M Kopf  
 Description: Connecting to existing 15 inch clay sewer north east corner of site

Field Management Professional

**DAILY SUMMARY REPORT**

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Tuesday, 08/02/2022



Transferred: 8/2/2022  
 Taken On: Aug 2 2022 9:35AM  
 Foreman: Anthony M Kopf  
 Description: Removing existing brick manhole

Daily MH Total:	42.00
Weekly MH Total:	67.00
Monthly MH Total:	67.00
ToDate MH Total:	699.50



Date: 08/08/2022  
Time: 03:59:28 PM

Field Management Professional

# DAILY SUMMARY REPORT

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Wednesday, 08/03/2022

Foreman ID: 10104		
Foreman Name: Anthony M Kopf		
Transferred On: 8/8/2022 3:59:27 PM		
Temperature & Weather:	Site Hours Worked:	Ground Conditions / Day Type:
AM: Rain (Light)    PM: Rain (Light)	From: 7:00 AM    To: 10:00 AM	Wet                      Cal Days: 678
High: 0 F    Low: 0 F    Precip: 0	Inspector: Quentin Jefferson	Work Day              Work Days: 29

**What did we do today?**

We installed 24 linear feet of 15 inch a 2000 sanitary sewer then we temporary flume the line and quit for the day because of rain The loader operator had a death in the family and was gone today and tomorrow so I just ran the loader backhoe

**Delays to Work/Project**

None

**Instructions Received**

Remove and replace sanitary sewer

**People Visiting the Job**

Quentin Jefferson

**Employee Summary**

Employee ID	Employee Name	Work Class	Regular Time	Over Time
10104	Anthony M Kopf	Laborer Foreman_Kopf	3.00	0.50
16208	Kenneth M Hurt	Laborer Pipesetter (Grp 2)	2.50	0.00
16255	Troy N Hoffman	Operator 150-3 (high level)	2.50	0.50
16328	Brady J Hill	Laborer Appr Yr 1 @ 75%	2.50	0.00
<b>Total Hours:</b>			10.50	1.00

**Equipment Summary**

Equipment ID	Description	Work Time
11151	Utility Bed Truck EXT Cab	3.00
14613	4X4 Loader-Extendahoe - CAT 420E	2.50
15168	Zero Swing Excavator - Komatsu PC138	2.50
<b>Total Hours:</b>		8.00

**Today's Quantities**

Cost Code	Description	Quantity Unit	Actual MH	Budgeted MH
99- 10-	Sewer Realignment Note:	0.01 LS	11.50	0.00
<b>Today's Total:</b>			11.50	0.00

**Diary Images**

Field Management Professional

## DAILY SUMMARY REPORT

Date: 08/08/2022

Time: 03:59:28 PM

Project ID: 21077-

Daily Diary Date:

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Wednesday, 08/03/2022



**Transferred:** 8/3/2022  
**Taken On:** Aug 3 2022 9:06AM  
**Foreman:** Anthony M Kopf  
**Description:** Uncovering existing lateral to be hooked back up later



**Transferred:** 8/3/2022  
**Taken On:** Aug 3 2022 8:31AM  
**Foreman:** Anthony M Kopf  
**Description:** Installing 15 inch a 2000



**Transferred:** 8/3/2022  
**Taken On:** Aug 3 2022 7:21AM  
**Foreman:** Anthony M Kopf  
**Description:** Compacting pipe bedding



# DAILY SUMMARY REPORT

Date: 08/08/2022

Time: 03:59:28 PM

Field Management Professional

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Wednesday, 08/03/2022

Daily MH Total:	11.50
Weekly MH Total:	78.50
Monthly MH Total:	78.50
ToDate MH Total:	711.00



QUALITY SINCE 1925

Field Management Professional

# DAILY SUMMARY REPORT

Date: 08/08/2022

Time: 04:05:29 PM

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Thursday, 08/04/2022

Foreman ID: 10104	Site Hours Worked:	Ground Conditions / Day Type:
Foreman Name: Anthony M Kopf	From: 7:00 AM To: 3:30 PM	Wet Cal Days: 678
Transferred On: 8/8/2022 4:05:28 PM	Inspector: Quentin Jefferson	Work Day Work Days: 30
Temperature & Weather:		
AM: Partly Cloudy PM: Partly Cloudy		
High: 0 F Low: 0 F Precip: 0		

**What did we do today?**  
 We installed 69 linear feet of 15 inch a 2000 I ran the loader backhoe

**Delays to Work/Project**  
 None

**Instructions Received**  
 Remove and Install 15 inch sanitary sewer

**People Visiting the Job**  
 Quentin Jefferson

**Employee Summary**

Employee ID	Employee Name	Work Class	Regular Time	Over Time
10104	Anthony M Kopf	Laborer Foreman_Kopf	8.00	0.50
16208	Kenneth M Hurt	Laborer Pipesetter (Grp 2)	8.00	0.00
16255	Troy N Hoffman	Operator 150-3 (high level)	8.00	0.50
16328	Brady J Hill	Laborer Appr Yr 1 @ 75%	8.00	0.00
<b>Total Hours:</b>			32.00	1.00

**Equipment Summary**

Equipment ID	Description	Work Time
11151	Utility Bed Truck EXT Cab	0.00
14613	4X4 Loader-Extendahoe - CAT 420E	0.00
15168	Zero Swing Excavator - Komatsu PC138	0.00
<b>Total Hours:</b>		0.00

**Today's Quantities**

Cost Code	Description	Quantity Unit	Actual MH	Budgeted MH
99- 10-	Sewer Realignment Note:	0.01 LS	33.00	0.00
<b>Today's Total:</b>			33.00	0.00

**Diary Images**

Field Management Professional

# DAILY SUMMARY REPORT

Date: 08/08/2022

Time: 04:05:29 PM

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Thursday, 08/04/2022



**Transferred:** 8/4/2022  
**Taken On:** Aug 4 2022 9:03AM  
**Foreman:** Anthony M Kopf  
**Description:** Compacting pipe bedding around a 2000mm



**Transferred:** 8/4/2022  
**Taken On:** Aug 4 2022 8:50AM  
**Foreman:** Anthony M Kopf  
**Description:** Excavating to install 15 inch a 2000mm



**Transferred:** 8/4/2022  
**Taken On:** Aug 4 2022 7:30AM  
**Foreman:** Anthony M Kopf  
**Description:** Uncovering another existing lateral



QUALITY SINCE 1925

Field Management Professional

# DAILY SUMMARY REPORT

Date: 08/08/2022

Time: 04:05:29 PM

Project ID: 21077-

Daily Diary Date:

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Thursday, 08/04/2022

Daily MH Total:	33.00
Weekly MH Total:	111.50
Monthly MH Total:	111.50
ToDate MH Total:	744.00



Field Management Professional

# DAILY SUMMARY REPORT

Date: 08/08/2022

Time: 04:42:13 PM

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Friday, 08/05/2022

Foreman ID: 10104		
Foreman Name: Anthony M Kopf		
Transferred On: 8/8/2022 4:42:12 PM		
Temperature & Weather:	Site Hours Worked:	Ground Conditions / Day Type:
AM: Sunny      PM: Sunny	From: 7:00 AM To: 3:30 PM	Dry      Cal Days: 678
High: 0 F Low: 0 F Precip: 0	Inspector: Quentin Jefferson	Work Day      Work Days: 31

**What did we do today?**

We installed 42 linear feet of 15 inch a 2000 and set and poured one manhole In the alleyway I also had a plumber from Crawford that hooked up three laterals per city spec the plumber was there for three hours

**Delays to Work/Project**

None

**Instructions Received**

Remove and replace 15 inch sanitary install manhole

**People Visiting the Job**

Plumber from Crawford, Quentin Jefferson

**Employee Summary**

Employee ID	Employee Name	Work Class	Regular Time	Over Time
10104	Anthony M Kopf	Laborer Foreman_Kopf	8.00	0.50
15805	James D Sawvel	Operator 150-3 (high level)	8.00	0.00
16208	Kenneth M Hurt	Laborer Pipesetter (Grp 2)	8.00	0.00
16255	Troy N Hoffman	Operator 150-3 (high level)	8.00	0.50
16328	Brady J Hill	Laborer Appr Yr 1 @ 75%	8.00	0.00
<b>Total Hours:</b>			40.00	1.00

**Equipment Summary**

Equipment ID	Description	Work Time
11151	Utility Bed Truck EXT Cab	8.00
14613	4X4 Loader-Extendahoe - CAT 420E	8.00
15168	Zero Swing Excavator - Komatsu PC138	8.00
<b>Total Hours:</b>		24.00

**Today's Quantities**

Cost Code	Description	Quantity Unit	Actual MH	Budgeted MH
99- 10-	Sewer Realignment Note:	0.01 LS	41.00	0.00
<b>Today's Total:</b>			41.00	0.00

Field Management Professional

# DAILY SUMMARY REPORT

Date: 08/08/2022

Time: 04:42:13 PM

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Friday, 08/05/2022

### Diary Images



Transferred: 8/5/2022  
Taken On: Aug 5 2022 3:01PM  
Foreman: Anthony M Kopf  
Description: Manhole in alleyway installed and laterals hooked up



Transferred: 8/5/2022  
Taken On: Aug 5 2022 3:01PM  
Foreman: Anthony M Kopf  
Description: Manhole in Alleyway installed and poured

**DAILY SUMMARY REPORT**

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Friday, 08/05/2022



**Transferred:** 8/5/2022  
**Taken On:** Aug 5 2022 10:21AM  
**Foreman:** Anthony M Kopf  
**Description:** Plumber from Crawford hooking up lateral



**Transferred:** 8/5/2022  
**Taken On:** Aug 5 2022 10:09AM  
**Foreman:** Anthony M Kopf  
**Description:** Supported phone line and installing 15 inch a 2000



**Transferred:** 8/5/2022  
**Taken On:** Aug 5 2022 7:45AM  
**Foreman:** Anthony M Kopf  
**Description:** Digging rock in alleyway for manhole installation

Field Management Professional

**DAILY SUMMARY REPORT**

Date: 08/08/2022

Time: 04:42:13 PM

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Friday, 08/05/2022



Transferred: 8/5/2022  
 Taken On: Aug 5 2022 7:17AM  
 Foreman: Anthony M Kopf  
 Description: Popping down water

Daily MH Total:	41.00
Weekly MH Total:	152.50
Monthly MH Total:	152.50
ToDate MH Total:	785.00

Field Management Professional

## DAILY SUMMARY REPORT

Date: 08/16/2022

Time: 09:55:16 AM

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Tuesday, 08/09/2022

Foreman ID: 10104	Foreman Name: Anthony M Kopf	Transferred On: 8/16/2022 9:55:15 AM
Temperature & Weather:	Site Hours Worked:	Ground Conditions / Day Type:
AM: Partly Cloudy PM: Partly Cloudy	From: 7:00 AM To: 3:30 PM	Wet Cal Days: 686
High: 0 F Low: 0 F Precip: 0	Inspector: Quentin	Work Day Work Days: 32

### What did we do today?

We finished backfilling around the manhole we installed on the south east corner of the job in the alleyway we also install the casting and flat top however I'm not sure what the finish elevation should be so we left it mostly uncovered at the very top then we moved to the north east corner of the job and removed The newly installed fire hydrant and 6 inch fire Hydrant leg per Nick Hecker

### Delays to Work/Project

None

### Instructions Received

None

### People Visiting the Job

Quentin with the city of Rock Island

### Employee Summary

Employee ID	Employee Name	Work Class	Regular Time	Over Time
10104	Anthony M Kopf	Laborer Foreman_Kopf	8.00	0.50
16255	Troy N Hoffman	Operator 150-3 (high level)	8.00	0.50
16328	Brady J Hill	Laborer Appr Yr 1 @ 75%	8.00	0.00
<b>Total Hours:</b>			24.00	1.00

### Equipment Summary

Equipment ID	Description	Work Time
11151	Utility Bed Truck EXT Cab	8.00
14613	4X4 Loader-Extendahoe - CAT 420E	8.00
15168	Zero Swing Excavator - Komatsu PC138	8.00
<b>Total Hours:</b>		24.00

### Today's Quantities

Cost Code	Description	Quantity Unit	Actual MH	Budgeted MH
99- 10-	Sewer Realignment	0.01 LS	13.00	0.00
	Note:			
99- 11-	Remove Newly Installed Hydrant & Leg	1.00 tm	12.00	0.00
<b>Today's Total:</b>			25.00	0.00

Diary Images

## DAILY SUMMARY REPORT

Project ID: 21077-

Daily Diary Date:


Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Tuesday, 08/09/2022

*Diary images*



Transferred: 8/9/2022  
Taken On: Aug 9 2022 10:12AM  
Foreman: Anthony M Kopf  
Description: Backfilled around manhole south east corner of job installed casting wasn't sure of an elevation though

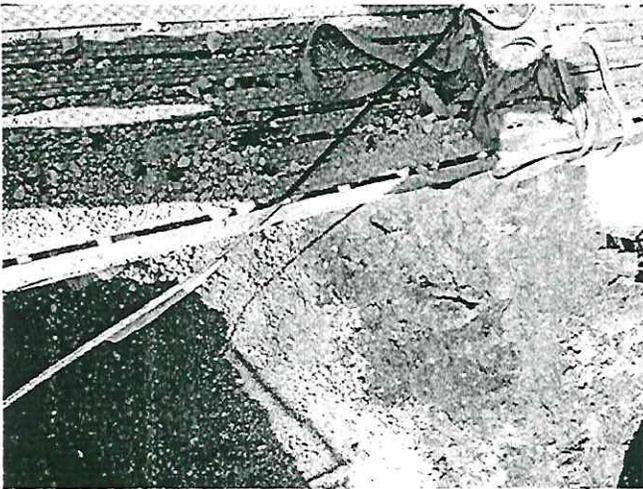

Transferred: 8/9/2022  
Taken On: Aug 9 2022 10:12AM  
Foreman: Anthony M Kopf  
Description: Removing phone cable support



Transferred: 8/9/2022  
Taken On: Aug 9 2022 10:26AM  
Foreman: Anthony M Kopf  
Description: Backfilling manhole south east corner of job

Field Management Professional

**DAILY SUMMARY REPORT**

Date: 08/16/2022

Time: 09:55:16 AM

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Tuesday, 08/09/2022



**Transferred:** 8/9/2022  
**Taken On:** Aug 9 2022 12:07PM  
**Foreman:** Anthony M Kopf  
**Description:** Removing newly installed fire hydrant north east corner of job:002

Daily MH Total:	25.00
Weekly MH Total:	25.00
Monthly MH Total:	177.50
ToDate MH Total:	810.00



Field Management Professional

# DAILY SUMMARY REPORT

Date: 10/31/2022  
Time: 08:52:56 PM

Project ID: 21077-

Daily Diary Date:

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Monday, 10/24/2022

Foreman ID: 10104		
Foreman Name: Anthony M Kopf		
Transferred On: 10/31/2022 8:52:56 PM		
Temperature & Weather:	Site Hours Worked:	Ground Conditions / Day Type:
AM: Partly Cloudy PM: Partly Cloudy	From: 7:00 AM To: 3:30 PM	Wet Cal Days: 762
High: 0 F Low: 0 F Precip: 0	Inspector: Quentin Washington	Work Day Work Days: 35

**What did we do today?**

We started the day with Joe Fiems getting our GPS to work then we staked out the 6 inch water service after that we dug and sat sanitary manhole north east corner of job however we had to cut 7 inches off the bottom of the manhole and we had to cut the dog houses in the manhole then we poured the invert and collars This was all T&m for the city of Rock Island

**Delays to Work/Project**

Getting the GPS to work

**Instructions Received**

Install sanitary sewer manhole

**People Visiting the Job**

Nick Hecker, Quentin Washington

**Employee Summary**

Employee ID	Employee Name	Work Class	Regular Time	Over Time
10104	Anthony M Kopf	Laborer Foreman_Kopf	8.00	1.00
16255	Troy N Hoffman	Operator 150-3 (high level)	8.00	1.00
16371	Quenton H Gard	Laborer Pipesetter (Grp 2)	8.00	0.50
<b>Total Hours:</b>			24.00	2.50

**Equipment Summary**

Equipment ID	Description	Work Time
11151	Utility Bed Truck EXT Cab	8.50
14613	4X4 Loader-Extendahoe - CAT 420E	2.00
15172	Zero Swing Excavator - Komatsu PC128	6.50
<b>Total Hours:</b>		17.00

**Today's Quantities**

Cost Code	Description	Quantity Unit	Actual MH	Budgeted MH
720800- -	6" DIP WATER Note:	0.01 lf	7.00	0.01
99- 10-	Sewer Realignment	0.70 LS	19.50	0.00
<b>Today's Total:</b>			26.50	0.01

Diary Images

Field Management Professional

# DAILY SUMMARY REPORT

Date: 10/31/2022  
Time: 08:52:57 PM

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Monday, 10/24/2022

*Diary images*



**Transferred:** 10/24/2022  
**Taken On:** Oct 24 2022 2:43PM  
**Foreman:** Anthony M Kopf  
**Description:** Pouring concrete for invert and collars



**Transferred:** 10/24/2022  
**Taken On:** Oct 24 2022 10:40AM  
**Foreman:** Anthony M Kopf  
**Description:** Cutting 7 inches off the bottom of the manhole because it was too tall



**Transferred:** 10/24/2022  
**Taken On:** Oct 24 2022 10:40AM  
**Foreman:** Anthony M Kopf  
**Description:** Getting ready to set manhole over sewer pipe north east corner of job



QUALITY SINCE 1925

Field Management Professional

# DAILY SUMMARY REPORT

Date: 10/31/2022

Time: 08:52:57 PM

Project ID: 21077-

Daily Diary Date:

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Monday, 10/24/2022

Daily MH Total:	28.00
Weekly MH Total:	28.00
Monthly MH Total:	51.00
ToDate MH Total:	861.00



Field Management Professional

# DAILY SUMMARY REPORT

Date: 10/31/2022

Time: 09:09:49 PM

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Wednesday, 10/26/2022

Foreman ID: 10104		
Foreman Name: Anthony M Kopf		
Transferred On: 10/31/2022 9:09:49 PM		
Temperature & Weather:	Site Hours Worked:	Ground Conditions / Day Type:
AM: Partly Cloudy    PM: Partly Cloudy	From: 7:00 AM    To: 3:30 PM	Dry                      Cal Days: 762
High: 0 F    Low: 0 F    Precip: 0	Inspector: Quentin Washington	Work Day                      Work Days: 36

**What did we do today?**

We installed the cone on the manhole that we set for the city TNM we also cut the top of the pipe out inside the manhole then we moved over and tapped the sewer main and installed the 8 inch lateral not six and connected it we used two 8 inch 45s and 4 foot of 8" A2000 and one 8x6 furnace We had to dig this up and expose it all by hand because we couldn't get the excavator down in there

**Delays to Work/Project**

Couldn't maneuver the excavator to dig had to hand dig The 8 inch lateral

**Instructions Received**

Install sewer

**People Visiting the Job**

Quinton Washington, Nick Hecker

**Employee Summary**

Employee ID	Employee Name	Work Class	Regular Time	Over Time
10104	Anthony M Kopf	Laborer Foreman_Kopf	8.00	0.50
16255	Troy N Hoffman	Operator 150-3 (high level)	8.00	0.50
16371	Quenton H Gard	Laborer Pipesetter (Grp 2)	8.00	0.00
<b>Total Hours:</b>			24.00	1.00

**Equipment Summary**

Equipment ID	Description	Work Time
11151	Utility Bed Truck EXT Cab	8.00
14613	4X4 Loader-Extendahoe - CAT 420E	0.00
15172	Zero Swing Excavator - Komatsu PC128	8.00
<b>Total Hours:</b>		16.00



Date: 10/31/2022

Time: 09:09:49 PM

Field Management Professional

## DAILY SUMMARY REPORT

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Wednesday, 10/26/2022

*Today's Quantities*

Cost Code	Description	Quantity Unit	Actual MH	Budgeted MH
566100- -	CUT IN TEE Note:	1.00 ea	10.00	25.30
601000- 006-	INSTALL 6" SANITARY	4.00 lf	10.50	4.60
99- 10-	Sewer Realignment	0.04 LS	4.50	0.00
<b>Today's Total:</b>			<b>25.00</b>	<b>29.90</b>

## DAILY SUMMARY REPORT

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Wednesday, 10/26/2022

*Diary Images*



Transferred: 10/26/2022  
 Taken On: Oct 26 2022 1:32PM  
 Foreman: Anthony M Kopf  
 Description: Sewer tap in lateral connection



Transferred: 10/26/2022  
 Taken On: Oct 26 2022 8:32AM  
 Foreman: Anthony M Kopf  
 Description: Installed con on sanitary manhole

Daily MH Total:	25.00
Weekly MH Total:	53.00
Monthly MH Total:	76.00
ToDate MH Total:	886.00



Date: 11/11/2022  
Time: 09:17:00 AM

Field Management Professional

## DAILY SUMMARY REPORT

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Thursday, 11/10/2022

Foreman ID: 10104  
Foreman Name: Anthony M Kopf  
Transferred On: 11/11/2022 9:16:59 AM

Temperature & Weather:

AM: Cloudy PM: Cloudy  
High: 0 F Low: 0 F Precip: 0

Site Hours Worked:

From: 7:00 AM To: 3:30 PM  
Inspector: Quentin Jefferson

Ground Conditions / Day Type:

Dry Cal Days: 773  
Work Day Work Days: 46

*What did we do today?*

Cleaned out area to set catch basin also installed hood inside catch basin over outflow and we set the catch basin and installed 2 foot of 15 inch a2000 between catch basin and combination sewer manhole then we poured collars on the catch basin and on the manhole and we also poured a fill it inside the manhole for the 15 inch we also had to cut the overhang on the base for the catch basin off because there wasn't enough room between the existing pipe and the manhole

*Delays to Work/Project*

None

*Instructions Received*

Install new catch basin west side of 17th St.

*People Visiting the Job*

Quentin Jefferson, Nick Hecker

*Employee Summary*

Employee ID	Employee Name	Work Class	Regular Time	Over Time
10104	Anthony M Kopf	Laborer Foreman_Kopf	8.00	0.50
16255	Troy N Hoffman	Operator 150-3 (high level)	8.00	0.50
16371	Quenton H Gard	Laborer Pipesetter (Grp 2)	8.00	0.00
<b>Total Hours:</b>			<b>24.00</b>	<b>1.00</b>

*Equipment Summary*

Equipment ID	Description	Work Time
01 Rental Equipm	Rental Equipment 01	0.00
11151	Utility Bed Truck EXT Cab	8.00
14613	4X4 Loader-Extendahoe - CAT 420E	0.00
15172	Zero Swing Excavator - Komatsu PC128	8.00
<b>Total Hours:</b>		<b>16.00</b>

*Today's Quantities*

Cost Code	Description	Quantity Unit	Actual MH	Budgeted MH
99- 13-	Catch Basin City of Rock Island Note:	1.00 LS	25.00	0.00
<b>Today's Total:</b>			<b>25.00</b>	<b>0.00</b>

Diary Images

**DAILY SUMMARY REPORT**

Date: 11/11/2022

Time: 09:17:00 AM

Field Management Professional

Project ID: 21077-

Daily Diary Date


Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Thursday, 11/10/2022


*Diary images*



**Transferred:** 11/10/2022  
**Taken On:** Nov 10 2022 2:59PM  
**Foreman:** Anthony M Kopf  
**Description:** Pouring collars on catch basin

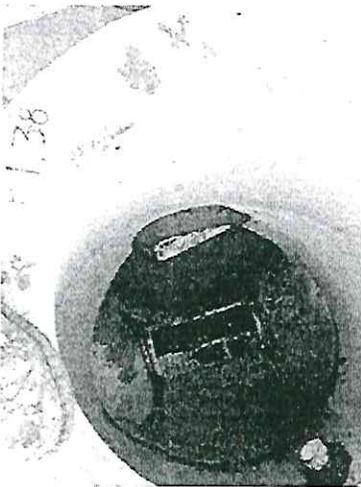

**Transferred:** 11/10/2022  
**Taken On:** Nov 10 2022 2:59PM  
**Foreman:** Anthony M Kopf  
**Description:** Poured collar and fill it in combination sewer manhole to accommodate pipe between manhole and catch basin

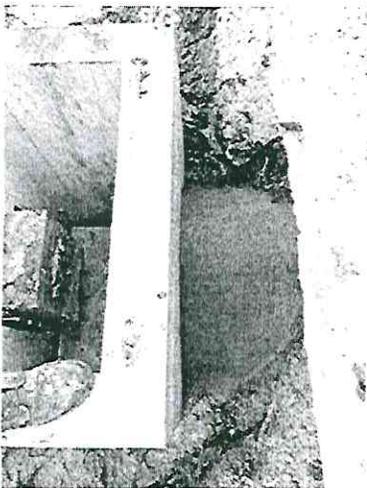

**Transferred:** 11/10/2022  
**Taken On:** Nov 10 2022 2:58PM  
**Foreman:** Anthony M Kopf  
**Description:** Poured collar on existing pipe and catch basin

Field Management Professional

# DAILY SUMMARY REPORT

Date: 11/11/2022


Time: 09:17:00 AM

Project ID: 21077-

Daily Diary Date

Project Name YWCA SITEWORK & UTILITIES (BUSH)

Date: Thursday, 11/10/2022

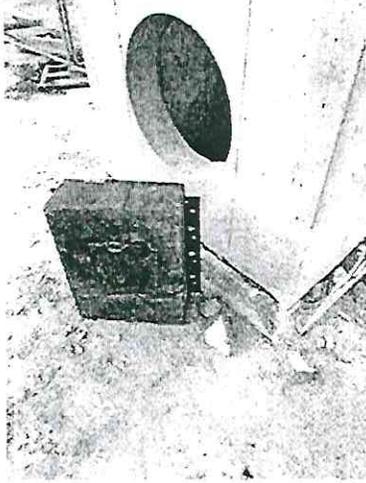

**Transferred:** 11/10/2022  
**Taken On:** Nov 10 2022 8:05AM  
**Foreman:** Anthony M Kopf  
**Description:** Installing hood inside catch basin on outflow pipe



**Transferred:** 11/10/2022  
**Taken On:** Nov 10 2022 8:04AM  
**Foreman:** Anthony M Kopf  
**Description:** Cutting opening in combination sewer manhole to run pipe from catch basin to manhole

<b>Daily MH Total:</b>	25.00
<b>Weekly MH Total:</b>	100.00
<b>Monthly MH Total:</b>	175.00
<b>ToDate MH Total:</b>	1,136.00
